


# Appendix C - PCL Project Schedule

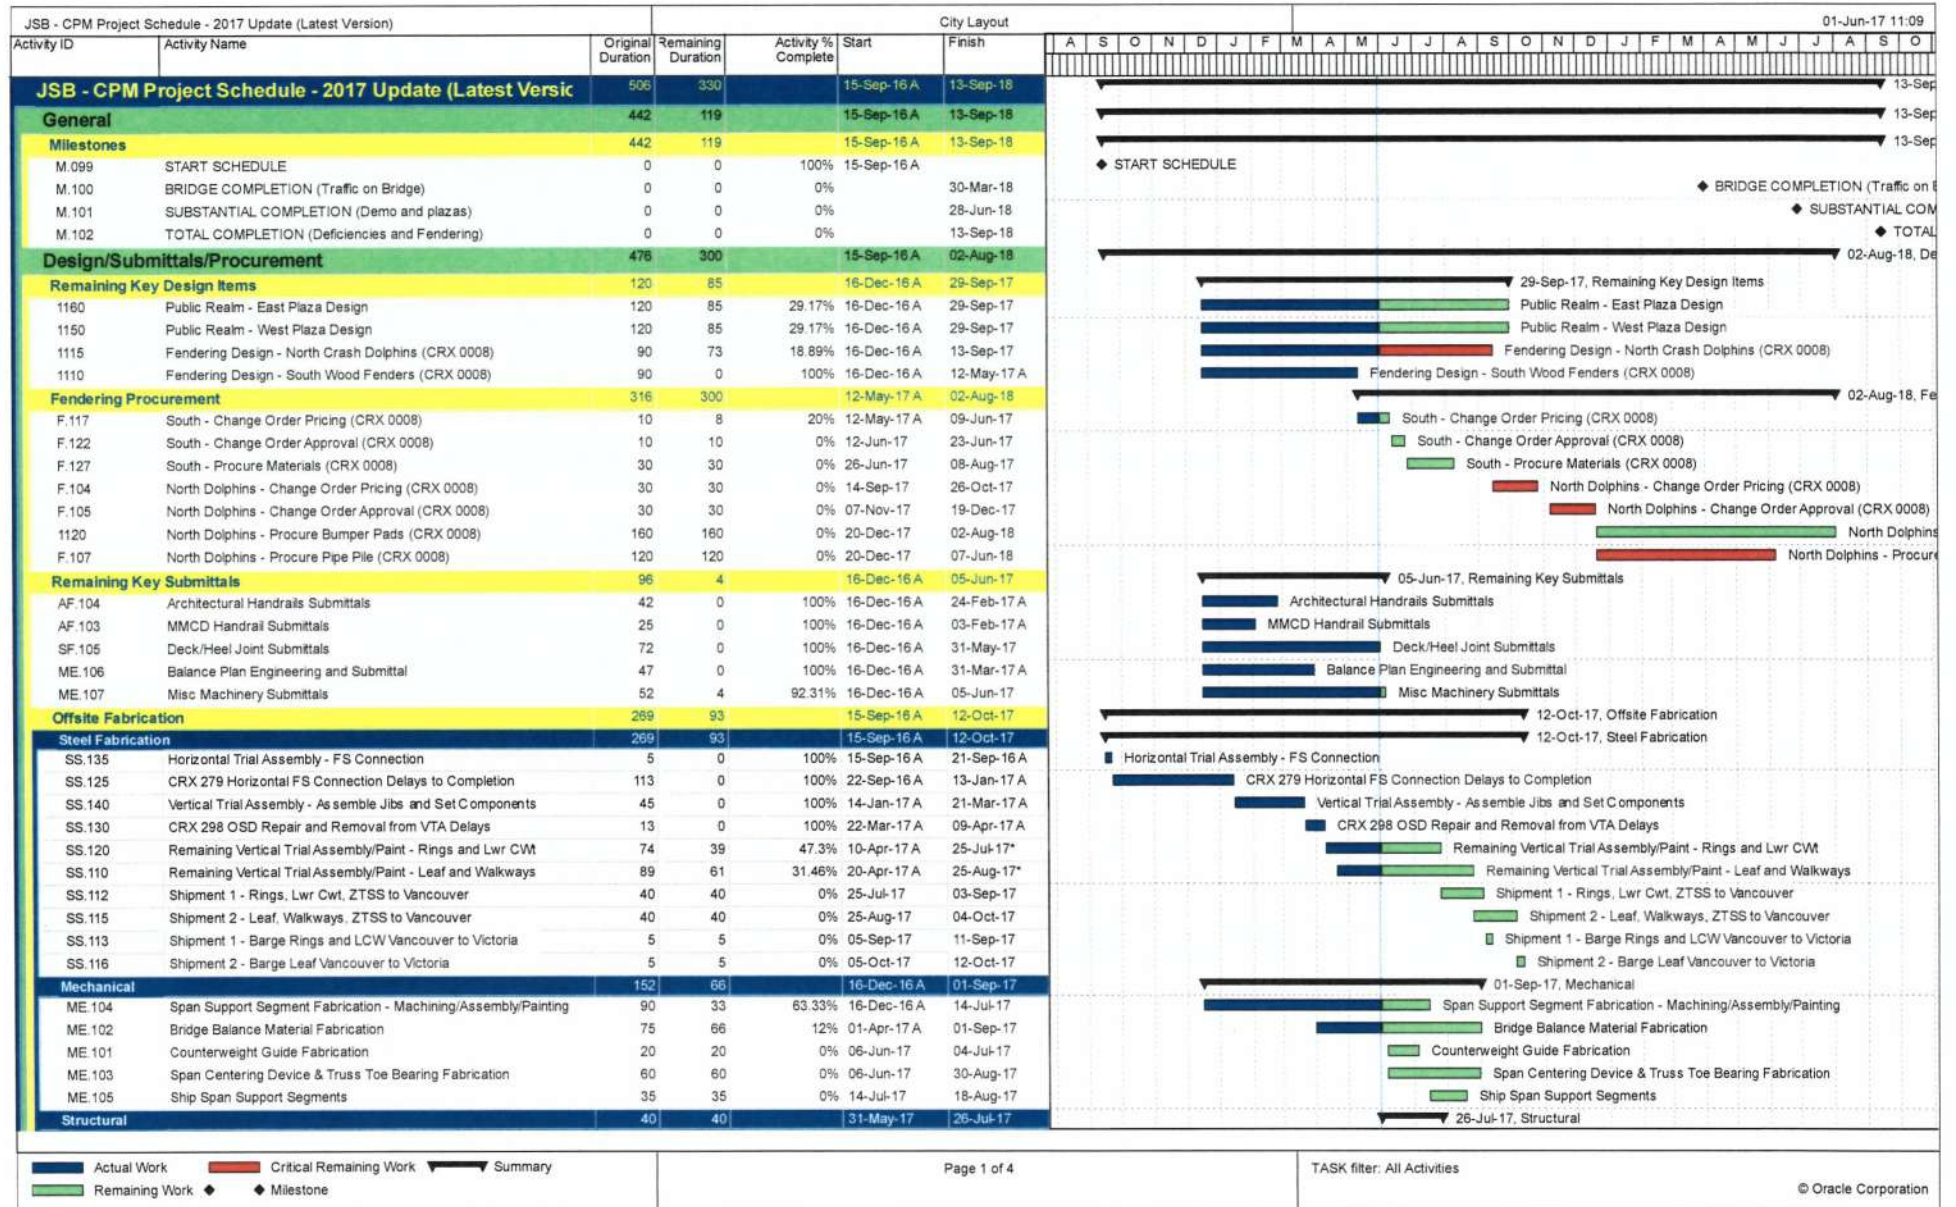

**JSB - CPM Project Schedule - 2017 Update (Latest Version)**

| Activity ID                              | Activity Name                                          | Original Duration | Remaining Duration | Activity % Complete | Start            | Finish           |
|------------------------------------------|--------------------------------------------------------|-------------------|--------------------|---------------------|------------------|------------------|
| SF.100                                   | Deck/Heel Joint Fabrication                            | 40                | 40                 | 0%                  | 31-May-17        | 26-Jul-17        |
| Architectural                            |                                                        | 136               | 67                 |                     | 07-Feb-17 A      | 05-Sep-17        |
| AF.100                                   | MMCD Handrail Fabrication                              | 20                | 0                  | 100%                | 07-Feb-17 A      | 15-Mar-17 A      |
| AF.101                                   | Architectural Handrails - Fabricate                    | 100               | 43                 | 57%                 | 27-Feb-17 A      | 31-Jul-17        |
| AF.102                                   | Aluminum Deck - Marcon Cut to Size                     | 70                | 70                 | 0%                  | 17-May-17 A      | 05-Sep-17        |
| <b>Bridge Works</b>                      |                                                        | <b>211</b>        | <b>211</b>         |                     | <b>31-May-17</b> | <b>30-Mar-18</b> |
| <b>Bascule Bridge</b>                    |                                                        | <b>211</b>        | <b>211</b>         |                     | <b>31-May-17</b> | <b>30-Mar-18</b> |
| <b>Bascule Leaf</b>                      |                                                        | <b>125</b>        | <b>125</b>         |                     | <b>12-Sep-17</b> | <b>10-Mar-18</b> |
| BL.1001                                  | Install Steel Erection Falsework - Rings and Lower Cwt | 10                | 10                 | 0%                  | 12-Sep-17        | 25-Sep-17        |
| <b>Prep Bascule Leaf on Barge</b>        |                                                        | <b>30</b>         | <b>30</b>          |                     | <b>13-Oct-17</b> | <b>24-Nov-17</b> |
| PL.100                                   | Prep and Install Traffic Coating                       | 15                | 15                 | 0%                  | 13-Oct-17        | 02-Nov-17        |
| PL.102                                   | Install End Bearings                                   | 5                 | 5                  | 0%                  | 03-Nov-17        | 09-Nov-17        |
| PL.101                                   | Install Electrical                                     | 15                | 15                 | 0%                  | 03-Nov-17        | 24-Nov-17        |
| <b>Channel Closure #1</b>                |                                                        | <b>5</b>          | <b>5</b>           |                     | <b>31-Oct-17</b> | <b>05-Nov-17</b> |
| C1.100                                   | Erect Rings & LCW                                      | 5                 | 5                  | 0%                  | 31-Oct-17        | 05-Nov-17        |
| <b>Between Closure #1 and Closure #2</b> |                                                        | <b>55</b>         | <b>55</b>          |                     | <b>26-Sep-17</b> | <b>14-Dec-17</b> |
| CC.1003                                  | Erect Leaf Falsework at Rest Pier                      | 5                 | 5                  | 0%                  | 26-Sep-17        | 02-Oct-17        |
| CC.1000                                  | Connect & Align Ring Assembly                          | 10                | 10                 | 0%                  | 06-Nov-17        | 20-Nov-17        |
| CC.1001                                  | Install Counterweights                                 | 30                | 30                 | 0%                  | 14-Nov-17        | 14-Dec-17        |
| CC.1002                                  | Erect Leaf Falsework at Ring                           | 5                 | 5                  | 0%                  | 21-Nov-17        | 27-Nov-17        |
| <b>Channel Closure #2</b>                |                                                        | <b>9</b>          | <b>9</b>           |                     | <b>14-Dec-17</b> | <b>23-Dec-17</b> |
| C2.102                                   | Remove Steel Erection Falsework                        | 9                 | 9                  | 0%                  | 14-Dec-17        | 23-Dec-17        |
| C2.101                                   | Install Panel D                                        | 9                 | 9                  | 0%                  | 14-Dec-17        | 23-Dec-17        |
| C2.100                                   | Erect Bascule Leaf                                     | 9                 | 9                  | 0%                  | 14-Dec-17        | 23-Dec-17        |
| <b>Walkway Install Closure #1</b>        |                                                        | <b>7</b>          | <b>7</b>           |                     | <b>27-Dec-17</b> | <b>04-Jan-18</b> |
| W1.105                                   | Weld OSD                                               | 5                 | 5                  | 0%                  | 27-Dec-17        | 02-Jan-18        |
| W1.101                                   | Install Section 1 PED Walkway                          | 4                 | 4                  | 0%                  | 27-Dec-17        | 01-Jan-18        |
| W1.100                                   | Install Section 1 MUD Walkway                          | 4                 | 4                  | 0%                  | 28-Dec-17        | 02-Jan-18        |
| W1.102                                   | Install Section 1 Aluminum Decking                     | 4                 | 4                  | 0%                  | 29-Dec-17        | 03-Jan-18        |
| W1.104                                   | Re-balance Span                                        | 1                 | 1                  | 0%                  | 04-Jan-18        | 04-Jan-18        |
| <b>Walkway Install Closure #2</b>        |                                                        | <b>6</b>          | <b>6</b>           |                     | <b>05-Jan-18</b> | <b>12-Jan-18</b> |
| W2.105                                   | Weld OSD                                               | 5                 | 5                  | 0%                  | 05-Jan-18        | 11-Jan-18        |
| W2.101                                   | Install Section 2 PED Walkway                          | 4                 | 4                  | 0%                  | 05-Jan-18        | 10-Jan-18        |
| W2.100                                   | Install Section 2 MUD Walkway                          | 4                 | 4                  | 0%                  | 05-Jan-18        | 10-Jan-18        |
| W2.102                                   | Install Section 2 Aluminum Decking                     | 3                 | 3                  | 0%                  | 08-Jan-18        | 10-Jan-18        |
| W2.103                                   | Re-balance Span                                        | 1                 | 1                  | 0%                  | 12-Jan-18        | 12-Jan-18        |
| <b>Walkway Install Closure #3</b>        |                                                        | <b>6</b>          | <b>6</b>           |                     | <b>15-Jan-18</b> | <b>22-Jan-18</b> |
| W3.105                                   | Weld OSD                                               | 5                 | 5                  | 0%                  | 15-Jan-18        | 19-Jan-18        |
| W3.101                                   | Install Section 3 PED Walkway                          | 4                 | 4                  | 0%                  | 15-Jan-18        | 18-Jan-18        |
| W3.100                                   | Install Section 3 MUD Walkway                          | 4                 | 4                  | 0%                  | 15-Jan-18        | 18-Jan-18        |
| W3.102                                   | Install Section 3 Aluminum Decking                     | 3                 | 3                  | 0%                  | 16-Jan-18        | 18-Jan-18        |
| W3.104                                   | Re-balance Span                                        | 1                 | 1                  | 0%                  | 22-Jan-18        | 22-Jan-18        |
| <b>Final Alignment &amp; Balance</b>     |                                                        | <b>47</b>         | <b>47</b>          |                     | <b>22-Jan-18</b> | <b>10-Mar-18</b> |
| BL.1003                                  | Final Balance Bascule Span                             | 22                | 22                 | 0%                  | 22-Jan-18        | 13-Feb-18        |
| BL.1004                                  | Final Alignment - Gear Tooth Alignment                 | 25                | 25                 | 0%                  | 13-Feb-18        | 10-Mar-18        |
| <b>Bascule Pier Concrete</b>             |                                                        | <b>62</b>         | <b>62</b>          |                     | <b>06-Nov-17</b> | <b>02-Feb-18</b> |
| MS.101                                   | Install Remaining Wheel Walkway Steel                  | 5                 | 5                  | 0%                  | 06-Nov-17        | 10-Nov-17        |
| MS.100                                   | Install Mask Slab Steel N&S                            | 5                 | 5                  | 0%                  | 06-Nov-17        | 10-Nov-17        |

**Legend:**

- Actual Work (Blue bar)
- Critical Remaining Work (Red bar)
- Summary (Black arrow)
- Remaining Work (Green bar)
- Milestone (Black diamond)

<

